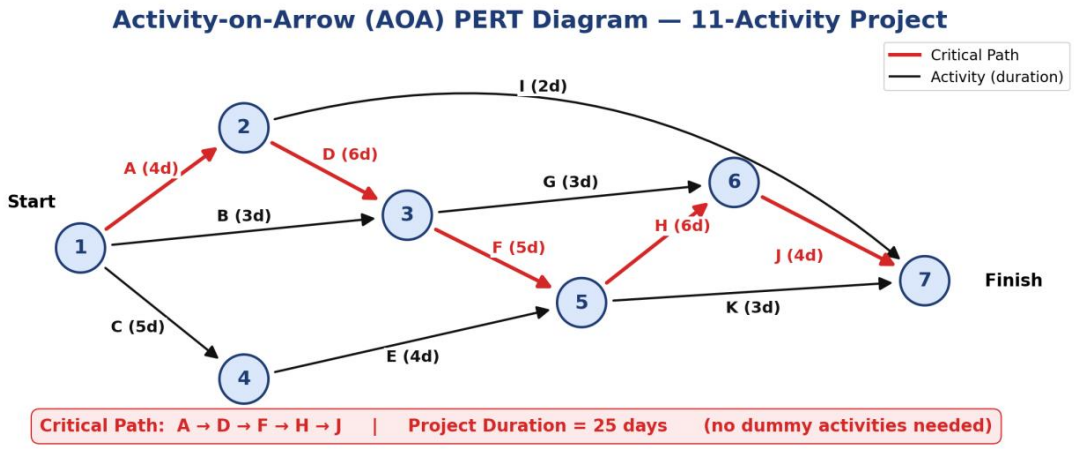
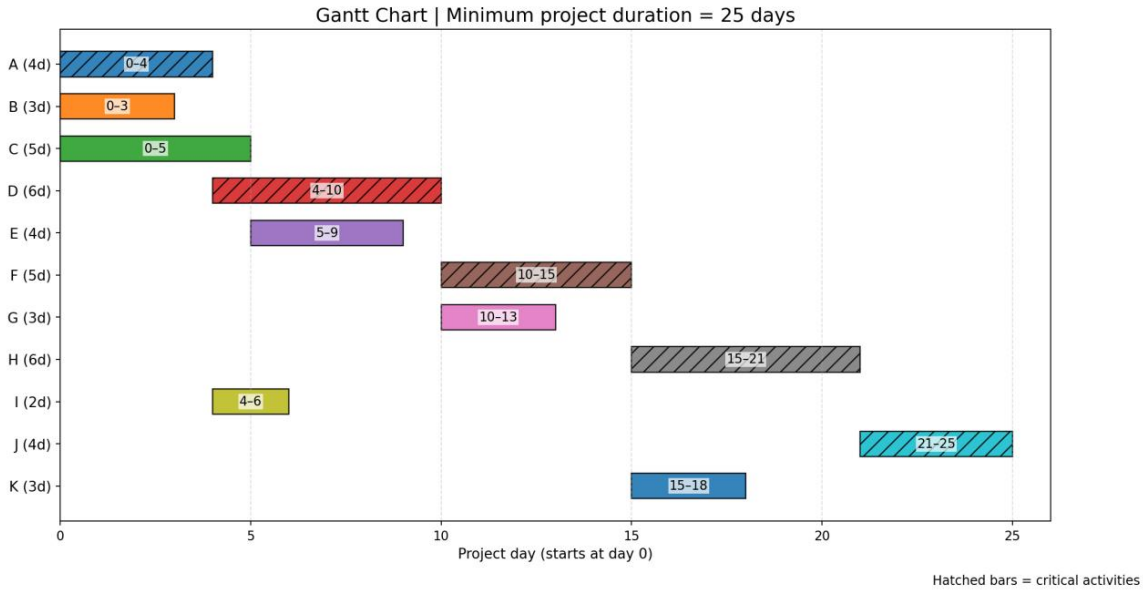
Second Task

Drav g activities:-

Activity	Predecessor
A	-
B	-
C	-
D	A
E	C
F	B, D
G	B, D
H	E, F
I	A
J	G, H
K	E, F

Task


Activity-on-Arrow (AOA) PERT Diagram — 11-Activity Project
Critical Path
Activity (duration)
Start
A (4d)
B (3d)
C (5d)
D (6d)
E (4d)
F (5d)
G (3d)
H (6d)
I (2d)
J (4d)
K (3d)
Finish
1
2
3
4
5
6
7
Critical Path: A → D → F → H → J | Project Duration = 25 days (no dummy activities needed)


Gantt Chart | Minimum project duration = 25 days
A (4d)
B (3d)
C (5d)
D (6d)
E (4d)
F (5d)
G (3d)
H (6d)
I (2d)
J (4d)
K (3d)
0–4
0–3
0–5
4–10
5–9
10–15
10–13
15–21
4–6
21–25
15–18
0
5
10
15
20
25
Project day (starts at day 0)
Hatched bars = critical activities
